




Presented by :
Group 5


Kerja.in



Group Member

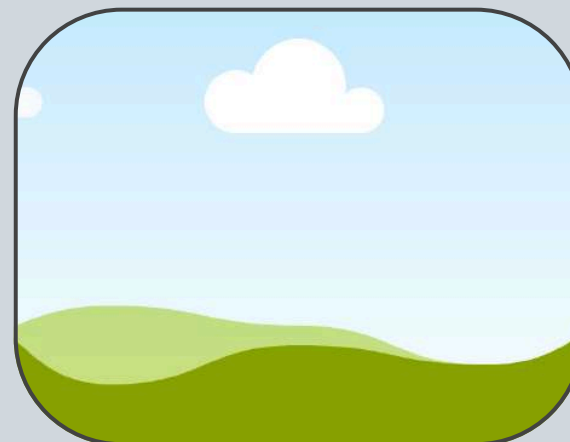

**AMANDA RIZKYTA PUTRI /
2702277345**

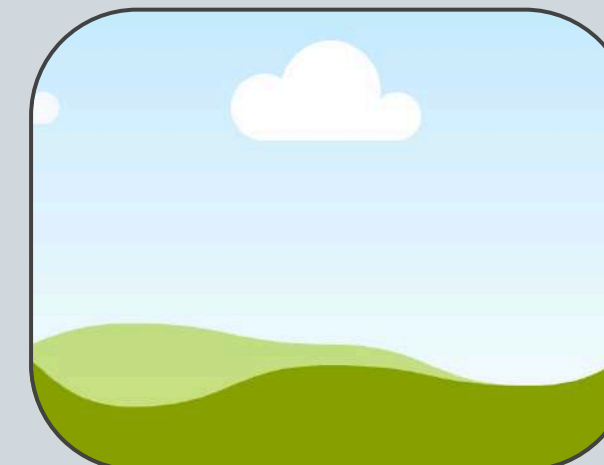


**BRYAN SURYA ADITAMA
HADIYANTO / 2702262482**



**DINY CHRISTIANTI /
2702368324**



**NAILA RAHMADINA /
2702360246**



**RENDI ODY SETIAWAN /
2702351765**



Study Case

IT Project: Kerja.in

Introduction Kerja.in

Kerja.in is a digital, job-training application designed to prepare fresh graduates to enter the professional workforce in a standardized manner and in line with industry needs. The platform offers a variety of video courses, real project-based training programs (project-based learning), and competency certifications that refer to the standards of the National Professional Certification Agency (BNSP).

In addition to training, Kerja.in also functions as a bridge between participants (talent) and employers through a talent pool system and job-matching services.





Executive Summary

The high unemployment rate among fresh graduates indicates a gap between the competencies gained through formal education and the real needs of the workplace. Many graduates possess strong theoretical knowledge but are not yet practically and professionally ready to enter the industry. On the other hand, companies also struggle to find entry-level candidates who are job-ready without requiring lengthy training.

Kerja.in was developed as a digital training platform focused on improving the job readiness of fresh graduates through structured video courses, real-world project simulations, soft-skill development, and competency certifications that refer to the standards of the National Professional Certification Agency (BNSP). Beyond being a learning platform, Kerja.in also serves as a bridge between participants and recruiters through a talent pool system and job-matching services.

This project aims to increase the employability of fresh graduates, accelerate company recruitment processes, and create a talent ecosystem that is more job-ready, standardized, and relevant to industry needs.

Background Current Challenges

01

The skills gap between fresh graduates and industry needs remains high.

02

Fresh graduates tend to lack practical work experience and exposure to real projects.

03

Industry-recognized competency certifications are not yet owned by most fresh graduates.

04

Companies spend significant time and costs on training entry-level candidates.




Opportunity



The high number of fresh graduates every year opens up huge opportunities for integrated job training platforms.



Companies need entry-level talent who are more technically and professionally ready to work.



Digital learning is increasingly accepted as a medium for competency development.



Competency certification based on the National Professional Certification Agency standards is an added value for job seekers.



Business case

IT Project: Kerja.in

Business Objectives

1

Improving the job readiness level of fresh graduates through structured training.

2

Increase the number of participants who pass national standards-based competency certification.

3

Accelerate the process of absorbing entry-level workers through a job matching system.

4

Reduce the time and initial training costs that the company must incur.

5

Increasing the competitiveness of fresh graduates in the job market through verified portfolios and certifications.

Proposed Solution

Skill Profilling

Mapping the skills of prospective workers

Smart Job Matching

Matching the skills profile of prospective workers with available job openings

Skill Upgrade Path

Provide training or certification recommendations based on job market needs

Expected Benefit

1. Improve Fresh Graduates' Job Readiness

Helps fresh graduates develop industry-relevant skills through training and certification.

2. Build a Trusted Talent Ecosystem

Provides verified profiles and certifications that increase recruiter confidence.

3. Reduce Recruitment Time and Costs

Enables companies to find qualified candidates faster and more efficiently.

4. Increase User Adoption Through Real Value

Delivers real value to both talents and recruiters, encouraging long-term engagement.

5. Establish a Strong Foundation for Future Growth

Creates a scalable platform that can expand its services and partnerships over time.

Success Metrics (KPIs – Kerja.in)

1

2

3

4

5

Monthly Active
Users (MAU)
≥ 5000 Users

Job Placement
Rate
> 100
Successful job
matches

Couser
Completion Rate
>500 Talents

Certification
pass rate
(standar Badan
Nasional
Sertifikasi
Profesi)
> 500 Talents

System
uptime ≥
99.5%

ROI (Initial Investment)

Component	Description	Cost (IDR)
UI/UX Design	Designing wireframes, prototypes, user flows, and high-fidelity interfaces	75,000,000
Frontend Development	Developing the web platform and dashboards for talents, recruiters, and administrators	180,000,000
Backend Development	Building the training system, certification system, job matching engine, and APIs	250,000,000
Database & Cloud Infrastructure	Database setup, cloud hosting, storage, backup, and server infrastructure	100,000,000
Training Content Development	Creating video courses, assessments, and project-based learning materials	150,000,000
Security Implementation	JWT/OAuth authentication, data encryption, and security testing	70,000,000
Testing & Quality Assurance	Unit testing, integration testing, UAT, and bug fixing activities	50,000,000
Deployment & Documentation	Server deployment, technical documentation, and user manuals	30,000,000
Project Management	Project coordination, sprint management, monitoring, and reporting	40,000,000
Contingency Reserve	Budget reserved for unexpected issues and minor scope adjustments	30,000,000
Total Investment		975,000,000

ROI (Estimated Benefit - Year 1)

Benefit Source	Assumption	Estimated Value (IDR)
Training & Certification Revenue	500 certified talents × Rp450,000 certification package	Rp225,000,000
Recruiter Subscription Revenue	25 companies × Rp1,250,000/month × 12 months	Rp375,000,000
Job Placement Revenue	100 successful job matches × Rp1,250,000 placement fee	Rp125,000,000
Featured Job Posting Revenue	100 premium job postings × Rp250,000	Rp25,000,000
Recruitment Efficiency Value	Cost savings generated for partner companies through faster hiring processes	Rp250,000,000
Total Estimated Benefit		Rp1,000,000,000

ROI Calculation

Formula

$$ROI = \frac{Total\ Benefit - Total\ Investment}{Total\ Investment} \times 100\%$$

Calculation

Total Benefit = Rp1,000,000,000

Total Investment = Rp975,000,000

$$ROI = \frac{Rp1,000,000,000 - Rp975,000,000}{Rp975,000,000} \times 100\%$$

$$ROI = \frac{Rp25,000,000}{Rp975,000,000} \times 100\%$$

$$ROI = 2.56\%$$

Based on the projected benefits and initial investment, Kerja.in is expected to generate an ROI of 2.56% during its first year of operation. While the return is relatively modest, this is reasonable because the first year focuses on platform development, content creation, user acquisition, and ecosystem building. The project is projected to reach its break-even point by the end of Year 1, while future growth in certified talents, recruiter subscriptions, and successful job placements is expected to significantly increase profitability in subsequent years.

ROI Summary

Item	Amount (IDR)
Total Investment	Rp975,000,000
Total Estimated Benefit	Rp1,000,000,000
Net Benefit	Rp25,000,000
ROI	256%
Break-Even Point	End of Year 1



Product Backlog

IT Project: Kerja.in

EPIC 1

User Registration & Profile Management

**Goal : Talents and recruiters can
create professional accounts
and profiles.**

	Priority	Story Point
As a talent, I would like to register an account so I can participate in the training program.	Hight	5
As a recruiter, I want to register a company account so I can search for candidates.	Hight	5
As a talent, I want to fill out a complete profile (CV, skills, portfolio) to look professional.	Hight	8
As a talent, I want to upload certificates to increase my credibility.	Medium	5
As an admin, I want to verify recruiter accounts to keep the platform trustworthy.	Hight	8

EPIC 2

Training & Standardization System

Goal: Preparing talent to be ready to work according to industry standards.

	Priority	Story Point
As a talent, I would like to see a list of available training.	Hight	5
As a talent, I would like to take the online training module.	Hight	8
As a system, I want to save the training progress of participants.	Hight	8
As an admin, I want to create and manage training modules.	Medium	13
As a talent, I would like to complete an assessment after training. Priority: High	Hight	8

EPIC 3

Certification System

Goal: To provide certification as proof of competence.

	Priority	Story Point
As a system, I want to issue automatic certificates if participants pass the assessment.	Hight	8
As a talent, I would like to download my certificate.	Hight	5
As a recruiter, I want to verify the authenticity of the candidate's certificate.	Hight	8
As an admin, I want to see the list of participants who passed.	Hight	5

EPIC 4

Job Matching & Recruitment

Goal : Connecting talent with job recruiters.

	Priority	Story Point
As a recruiter, I want to post a job opening.	Hight	8
As a talent, I would like to apply for a job through the platform.	Hight	8
As a system, I want to display candidate recommendations according to recruiter needs.	Medium	13
As a system, I want to recommend jobs according to talent skills.	Medium	13
As a recruiter, I want to contact candidates via chat system.	Medium	8

EPIC 5

Performance Tracking & Rating

Goal: Maintaining the quality and professionalism of talent.

	Priority	Story Point
As a recruiter, I want to rate the talent after the project is completed.	Medium	5
As a talent, I want to see feedback from recruiters.	Medium	5
As an admin, I want to monitor the overall performance of the talent.	Medium	8

EPIC 6

Analytics & Dashboard

Goal : Monitoring system and user performance.

	Priority	Story Point
As an admin, I want to see the dashboard of the number of active talents.	Medium	5
As an admin, I would like to see the number of certified talents.	Medium	5
As an admin, I want to see the number of successful job matches.	Hight	8

EPIC 7

Security & System Stability

Goal: Maintain system security and stability.

	Priority	Story Point
As a system, I want to login using secure authentication (JWT / OAuth).	Critical	8
As a system, I want the data stored encrypted.	Critical	8
As a DevOps, I want a scalable system for many users.	Hight	13

Epic Overview

Epic	Description
User Management	Registrasi & pengelolaan akun talent dan recruiter
Training System	Modul pelatihan & standarisasi kompetensi
Certification System	Assessment & penerbitan sertifikat
Job Matching	Posting lowongan & pencocokan talent
Performance Tracking	Rating & feedback pasca proyek
Analytics	Dashboard monitoring sistem
Security & Infrastructure	Keamanan dan kestabilan sistem

Master Product Backlog

ID	Epic	User Story	Priority	Story Point
PB01	User Management	Talent registration	High	5
PB02	User Management	Recruiter registration	High	5
PB03	User Management	Talent complete profile	High	8
PB04	User Management	Verify recruiter account	High	8
PB05	Training System	View training list	High	5
PB06	Training System	Enroll & access training module	High	8
PB07	Training System	Track participant progress	High	8
PB08	Training System	Admin manage training content	High	13
PB09	Certification	Automatic certificate generation	High	8
PB10	Certification	Download certificate	High	5

ID	Epic	User Story	Priority	Story
PB11	Certification	Certificate verification by recruiter	High	8
PB12	Job Matching	Post job vacancy	High	8
PB13	Job Matching	Apply job	High	8
PB14	Job Matching	Candidate recommendation engine	Medium	13
PB15	Job Matching	Job recommendation for talent	Medium	13
PB16	Performance	Rating & feedback system	Medium	5
PB17	Analytics	Admin dashboard (talent, job match, certification)	Medium	8
PB18	Security	Secure authentication system	Critical	8
PB19	Infrastructure	Scalable server setup	High	13
PB20	QA	Regression testing before release	Critical	8



Sprint Planning

IT Project: Kerja.in

SPRINT 1

Core Foundation & User System

Sprint Goal:

Building a registration, authentication and basic profile system for talents and recruiters

Deliverables:

- Login and registration systems active
- Talent and recruiter profiles
- Basic security systems in place
- Platform ready for use

ID	Story	SP
PB01	Talent registration	5
PB02	Recruiter registration	5
PB03	Talent profile management	8
PB05	Recruiter verification	8
PB21	Secure authentication	8
PB22	Data encryption	8

Total 42 sp

SPRINT 2

Training & Certification System

Sprint Goal:

BuildinProvides training modules and certification systems.

Deliverables:

- Training modules are accessible
- Progress is recorded
- Assessment system is running

ID	Story	SP
PB06	List training programs	5
PB07	Access training module	5
PB08	Save training progress	5
PB09	Admin manage training module	13
PB10	Online assessment	8

Total 36 sp

SPRINT 3

Certification & Job Marketplace

Sprint Goal:

Mengaktifkan sertifikasi dan fitur pencarian kerja.

Deliverables:

- Deliverables:
- Sertifikat otomatis terbit
- Recruiter bisa posting lowongan
- Talent bisa apply pekerjaan

ID	Story	SP
PB11	Auto certificate generation	8
PB12	Download certificate	5
PB13	Certificate verification	8
PB14	Job posting	8
PB15	Apply job	8

Total 37 sp

SPRINT 4

Matching, Performance & Analytics

Sprint Goal:

Elmproving the system with recommendations, ratings and monitoring

Deliverables:

- Smart matching active
- Rating system running
- Monitoring dashboard available
- Platform ready to launch

ID	Story	SP
PB16	Auto certificate generation	8
PB17	Download certificate	13
PB18	Certificate verification	5
PB19	Job posting	5
PB20	Apply job	8

Total 39 sp



Project Charter

IT Project: Kerja.in

Project purpose

The purpose of this project is to develop a digital platform that prepares talents through structured training and certification programs and connects them with recruiters, ensuring professional standards, competency validation, and efficient job matching.

Project Objectives

- Develop a functional online training and certification platform.
- Certify at least 500 talents within the first 6 months after launch.
- Connect certified talents with recruiters through a job matching system.
- Reduce recruitment time by 30% for participating companies.
- Achieve at least 80% user satisfaction rate from talents and recruiters.

Project Scope

IN SCOPE

- User registration (talent & recruiter)
- Profile management system
- Online training module system
- Online assessment & certification system
- Certificate verification feature
- Job posting and job application feature
- Basic recommendation system
- Dashboard for admin, talent, and recruiter
- Security system (authentication & encryption)
- System testing and deployment

OUT OF SCOPE

- Offline training programs
- Physical certification issuance
- Integration with external government employment systems
- Payroll management system
- Advanced AI-based recruitment analytics

Higher Level Requirement

- System must support at least 5,000 active users in the first phase.
- Certification system must automatically generate digital certificates.
- Recruiters must be able to verify certificate authenticity.
- Secure login system (JWT/OAuth based authentication).
- System uptime minimum 99%.
- Job application status must be trackable in real-time.

HighLevel Risk

- Low user adoption rate.
- Delay in training content development.
- Technical integration issues between modules.
- Data security breaches.
- Recruiters not actively using the platform.
- Budget overrun due to additional feature requests.

Timeline

Start Date: 1 March 2026
End Date: 30 April 2026
Platform Launch: 1 May 2026
Total Duration: 3 Months

Estimated Budget

Total Estimated Budget:
Rp 975.0000.000

Key Stakeholders

- Project Sponsor: Business Owner / Investor
- Project Manager: IT Project Manager
- Development Team (Frontend & Backend)
- UI/UX Designer
- QA & Tester
- Training Content Team
- Recruiters / Partner Companies
- Talents (Platform Users)

Project Manger Authority Succes Criteria

The Project Manager has authority to: Assign project tasks to team members Manage project schedule Control scope changes within agreed limits Manage approved budget allocation Coordinate between technical and business teams Approve minor technical and operational decisions

The project will be considered successful if: Platform is delivered within scope, time, and budget. At least 500 talents complete certification within 6 months. At least 100 successful job matches occur in the first year. No major security breach occurs. User satisfaction rate exceeds 80%.






WBS

IT Project: Kerja.in

KERJA.IN

Digital Job-Training & Job Matching Platform

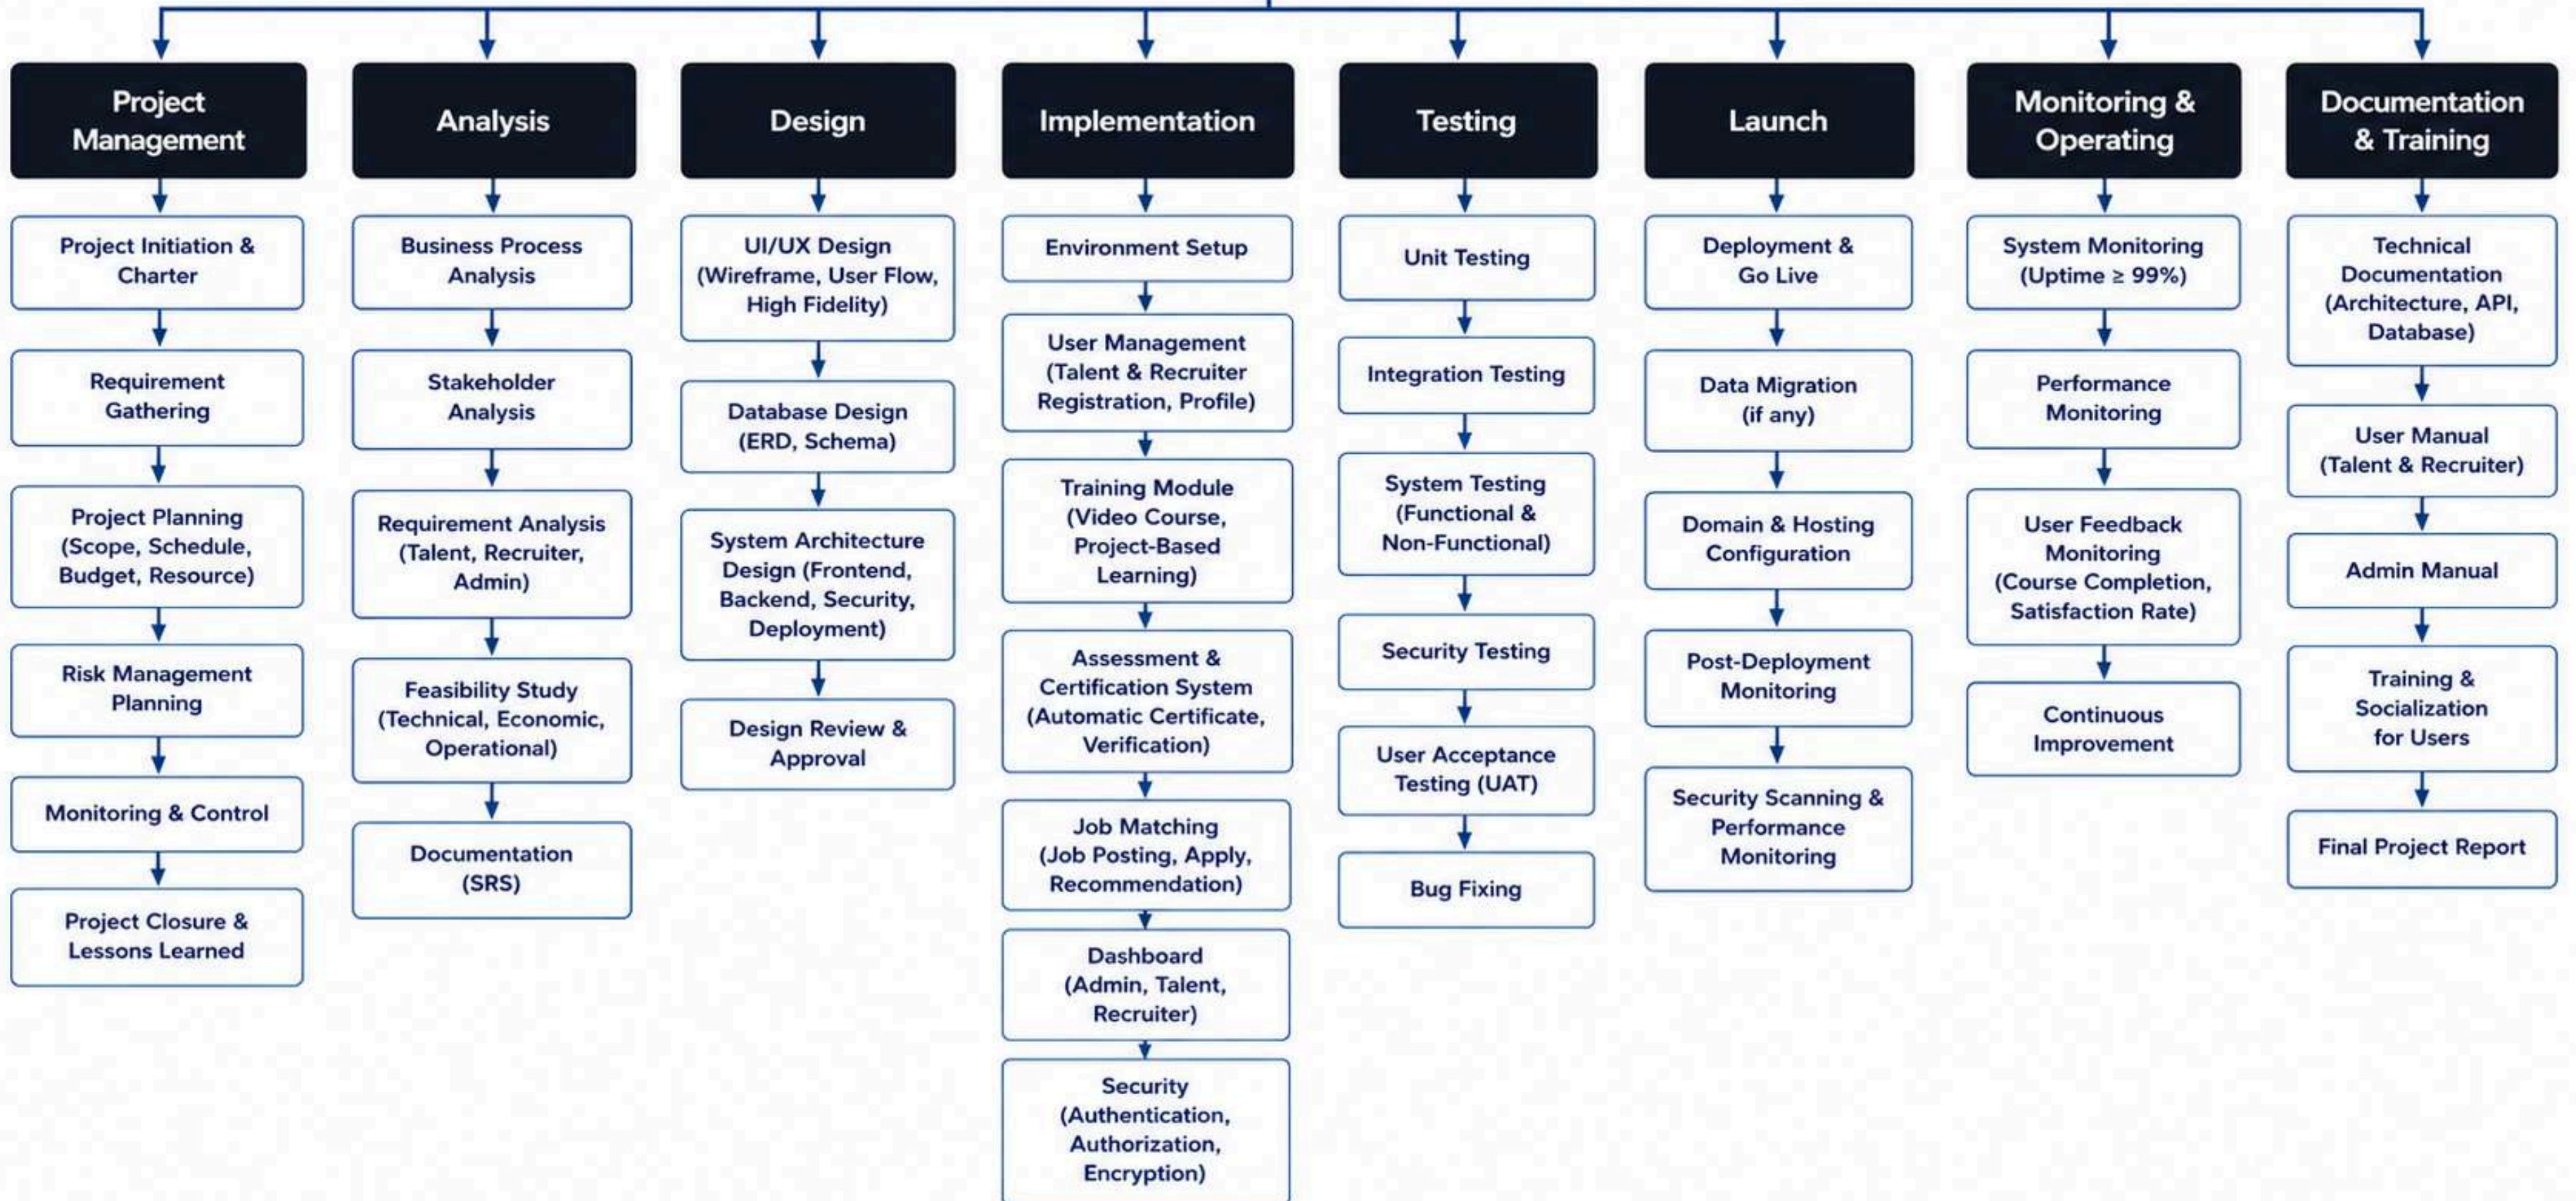

Initiation

Project Charter Development

- Identifikasi tujuan proyek
- Identifikasi stakeholder
- Penentuan scope awal

Requirement Gathering

- Wawancara stakeholder
- Analisis kebutuhan talent
- Analisis kebutuhan recruiter
- Dokumentasi kebutuhan sistem

Feasibility Study

- Technical feasibility
- Economic feasibility
- Operational feasibility

Planning

Project Planning

- Penyusunan WBS
- Penyusunan jadwal proyek
- Penyusunan anggaran proyek

Risk Management Planning

- Identifikasi risiko
- Analisis risiko
- Penyusunan mitigation plan

Resource Planning

- Penentuan tim proyek
- Pembagian tugas
- Estimasi kebutuhan infrastruktur

Development

Business Process Analysis

- Analisis proses pelatihan
- Analisis proses sertifikasi
- Analisis proses rekrutmen

UI/UX Design

- Wireframe
- User Flow
- High Fidelity Design
- Prototype Testing

Database Design

- ERD
- Database Schema
- Data Dictionary
-

System Architecture Design

- Frontend Architecture
- Backend Architecture
- Security Architecture
- Deployment Architecture

Testing

Unit Testing

- User Module
- Training Module
- Certification Module
- Job Matching Module

Integration Testing

- Frontend & Backend
- Database Integration

System Testing

- Functional Testing
- Non-Functional Testing

Security Testing

- Authentication Test
- Authorization Test
- Vulnerability Test

UAT

- UAT Preparation
- UAT Execution
- Feedback Collection

Bug Fixing

- Minor Bugs
- Major Bugs

Deployment

- Production Server Setup
- Database Migration
- Application Deployment
- Domain & Hosting Configuration
- Go Live
- Post Deployment Monitoring
- Security Scanning (SAST)

Closing

- Final Project Delivery
- Client Acceptance Sign-Off
- Resource Release
- Contract Closure
- Handover to Operations
- Lessons Learned Register
- Project Closure Report

Project Review

- **KPI Evaluation**
- **Schedule Performance Review**
- **Budget Performance Review**
- **Risk Review**
- **Sprint Retrospective**
- **Analisis Risiko Pasca-Rilis (Post-Launch Risk)**
- **User Satisfaction Evaluation**
- **Lessons Learned**

Documentation

- **Software Requirement Specification (SRS)**
- **System Design Documentation**
- **Database Documentation**
- **Technical Documentation**
- **API Documentation**
- **Testing Documentation**
- **User Manual**
- **Admin Manual**
- **Final Project Report**



Project Schedule

IT Project: Kerja.in


Project Schedule

ID	Task	Duration	Dependency
1	Project Initiation & Requirement	5 days	-
2	Feasibility Study & Project Planning	4 days	1
3	Project Initiation & Requirement	5 days	2
4	UI/UX Design	8 days	3
5	Database Design	5 days	3
6	System Architecture Design	4 days	3
7	User Authentication Module	5 days	4,5,6
8	Video Course Feature Development	8 days	7
9	Project-Based Learning Module	7 days	7
10	Competency Certification Feature	6 days	7
11	Talent Pool System Development	7 days	8,9,10
12	Job Matching Feature Development	8 days	11
13	Admin Dashboard Development	6 days	8,9,10
14	System Integration	5 days	12,13
15	Testing & Bug Fixing	7 days	14
16	User Acceptance Testing (UAT)	4 days	15
17	Deployment & Launch	3 days	16
18	Training & Documentation	3 days	17

Gantt chart Kerja.in

NAME		COMPANY NAME	
PROJECT MANAGER		DATE	


							PHASE ONE															
TASK ID	TASK TITLE	TASK OWNER	START DATE	DUE DATE	DURATION	PCT OF TASK COMPLETE	WEEK 1					WEEK 2					WEEK 3					
							M	T	W	R	F	M	T	W	R	F	M	T	W	R	F	M
1	Project Initiation & Requirement Gathering		25 May 2026	28 May 2026	5																	
1.1	Feasibility Study & Project Planning	Leon W	29 May 2026	4 Jun 2026	4	100%																
1.1.1	System Analysis	Kylie R	5 Jun 2026	16 Jun 2026	5	100%																
1.2	UI/UX Design	Pete S	5 Jun 2026	11 Jun 2026	8	90%																
1.3	Database Design	Steve L	5 Jun 2026	10 Jun 2026	5	40%																
1.4	System Architecture Design	Allen W	17 Jun 2026	23 Jun 2026	4	70%																
1.5	User Authentication Module Development	Malik M	24 Jun 2026	3 Jul 2026	5	60%																
1.6	Video Course Feature Development	Malik M	24 Jun 2026	2 Jul 2026	8	50%																
2	Project-Based Learning Module Development		24 Jun 2026	1 Jul 2026	7																	
2.1	Talent Pool System Development	Steve L	6 Jul 2026	14 Jul 2026	6	5%																
2.2	Job Matching Feature Development	Allen W	15 Jul 2026	24 Jul 2026	7	30%																

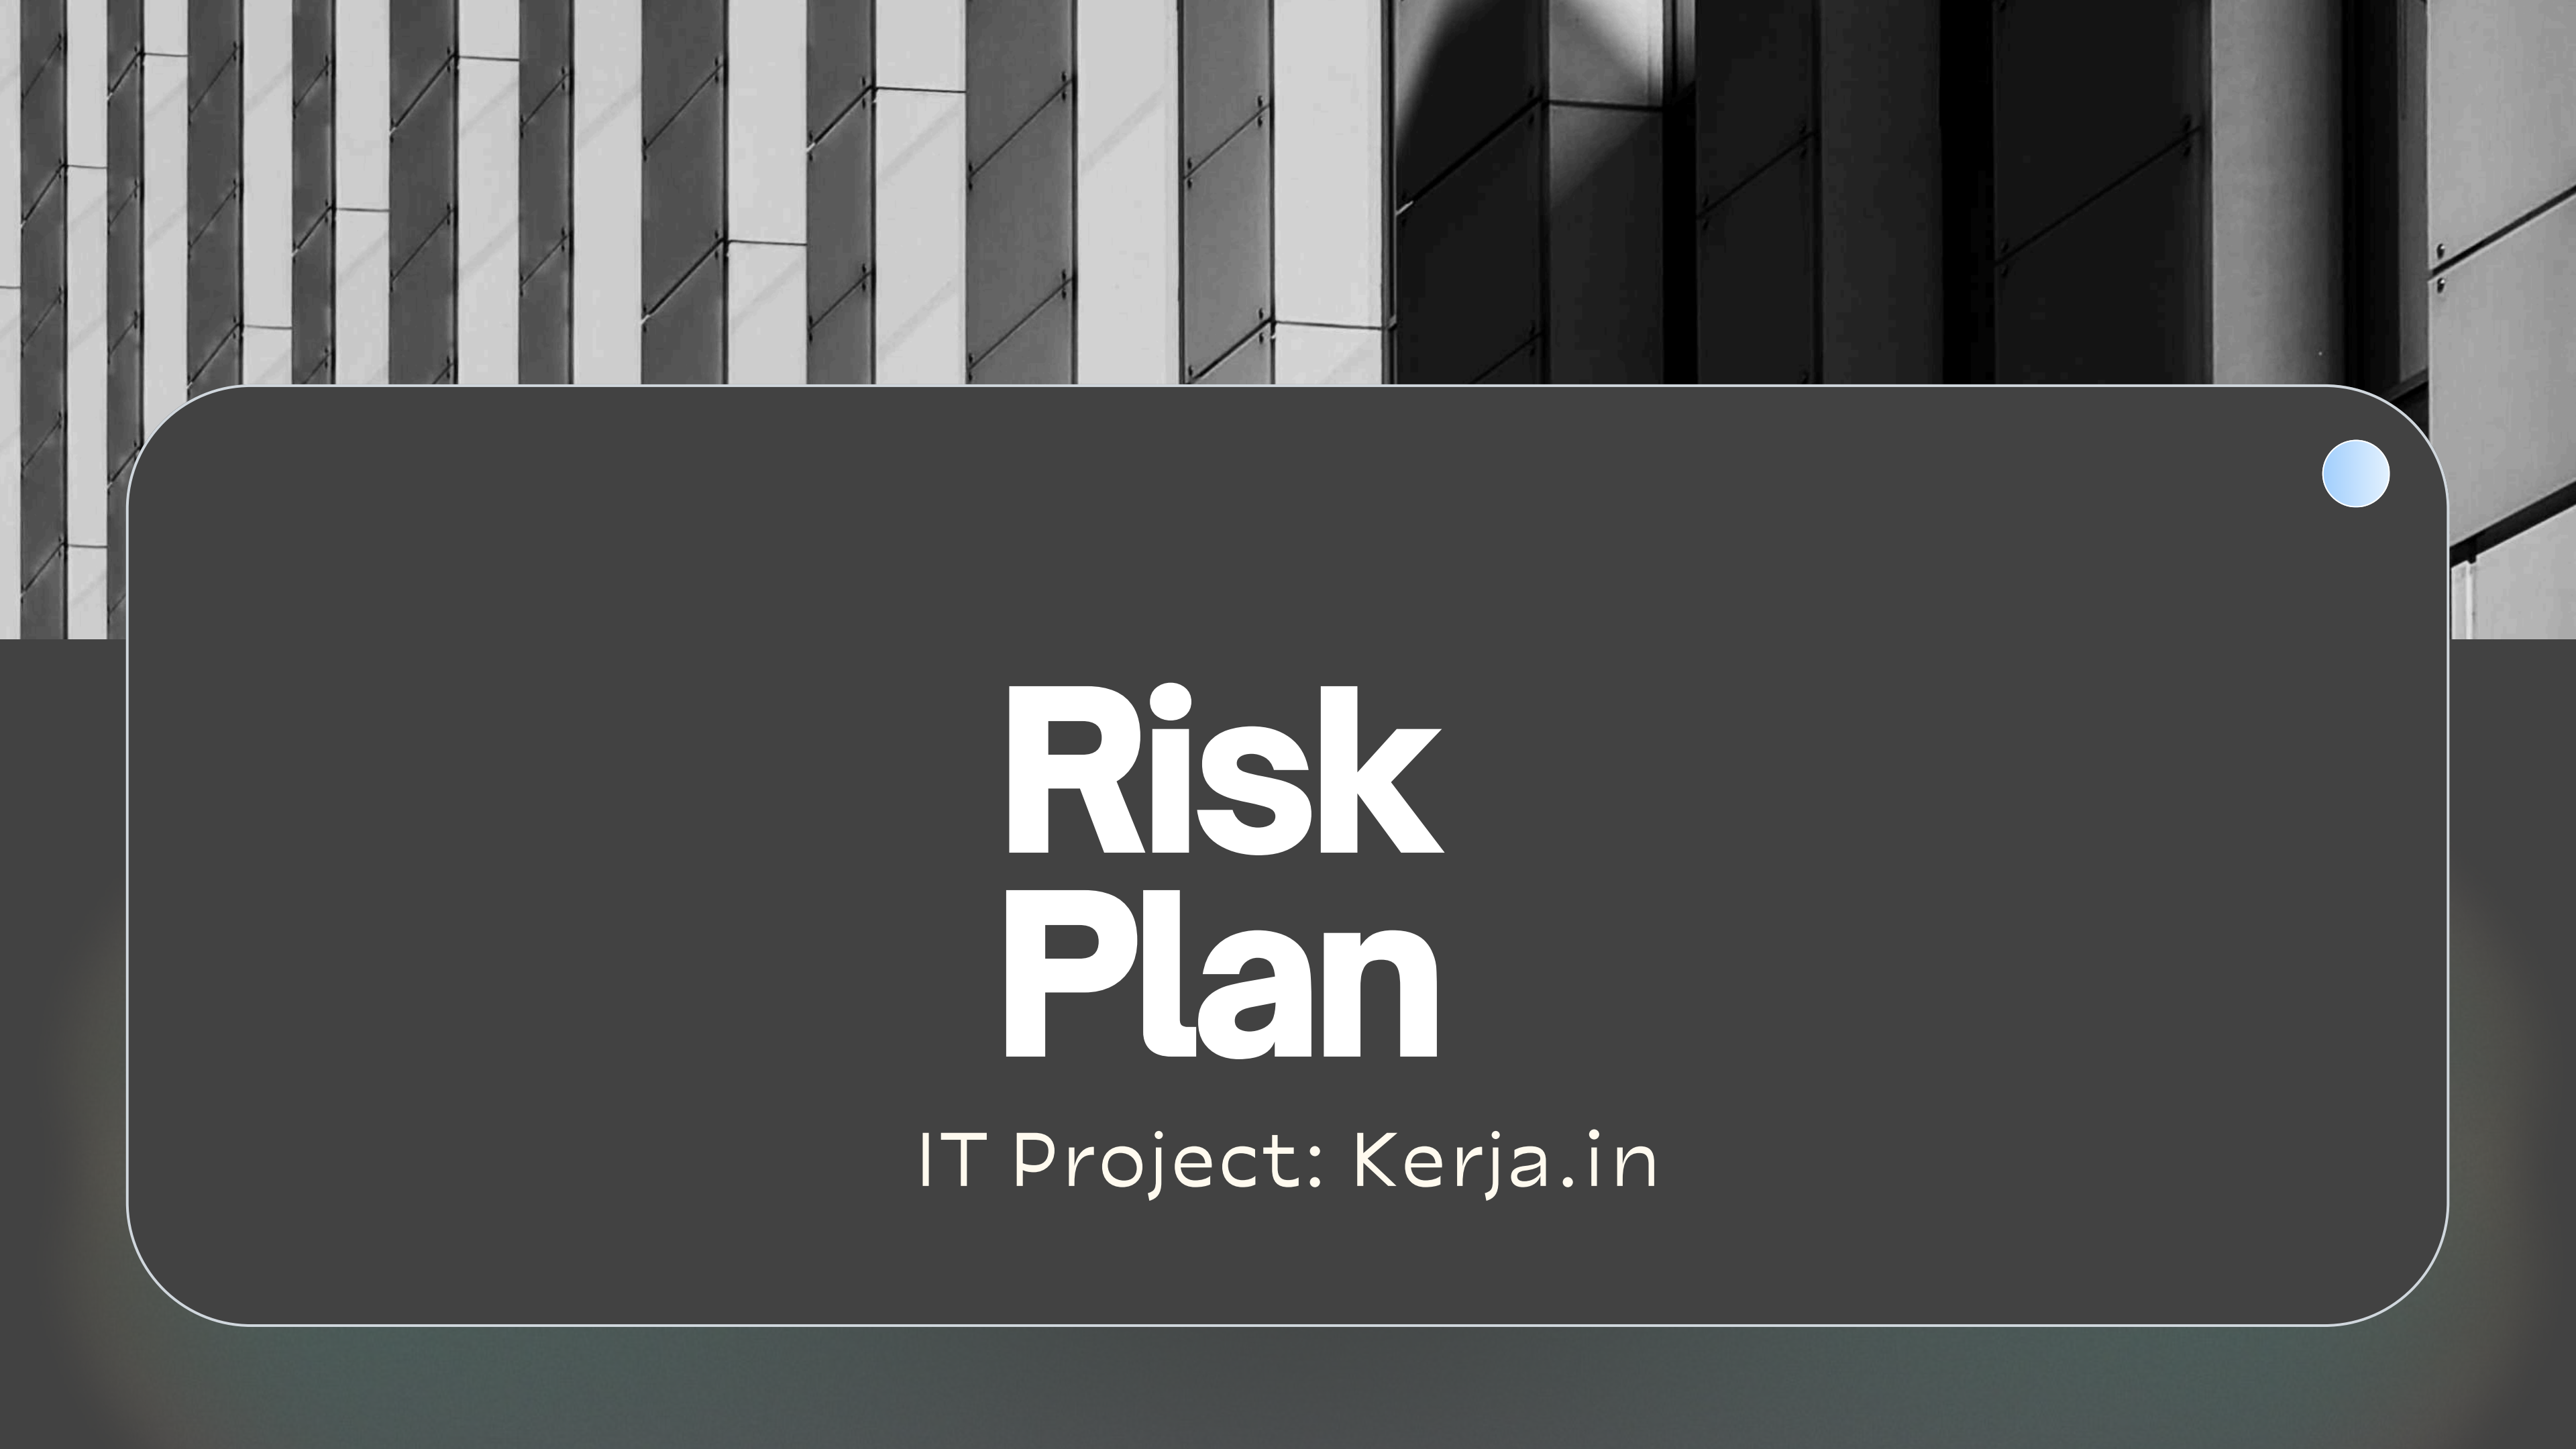

Risk Plan


IT Project: Kerja.in

Risk	Probability	Impact	Risk Level	Mitigation
Adoption rates are low and recruiters are not actively using the platform.	Medium	High	High	Provide various features that attract new users and design an optimal and easy-to-use UI/UX design.
Cost/budget overruns due to requests for additional features	Low	Medium	Low	Controlling scope changes to keep them within agreed boundaries
Technical integration issues between modules as well as unstable APIs	Medium	High	High	Allocate dedicated time for System Integration and perform Regression testing before launch.
Data security breaches or suboptimal user data protection	Low	High	Medium	Implement a secure authentication system based on JWT/OAuth and store data encrypted.
Unstable system performance / downtime due to less scalable system architecture when the number of users increases.	Low	High	Medium	Assign DevOps to design a scalable server architecture for multiple users to maintain a minimum system uptime of 99% to >99.5%\$
Low digital skills	Low	Medium	Low	Ensuring the UI/UX Design stage in the Planning phase produces an interface that is very user-friendly and easy to use.

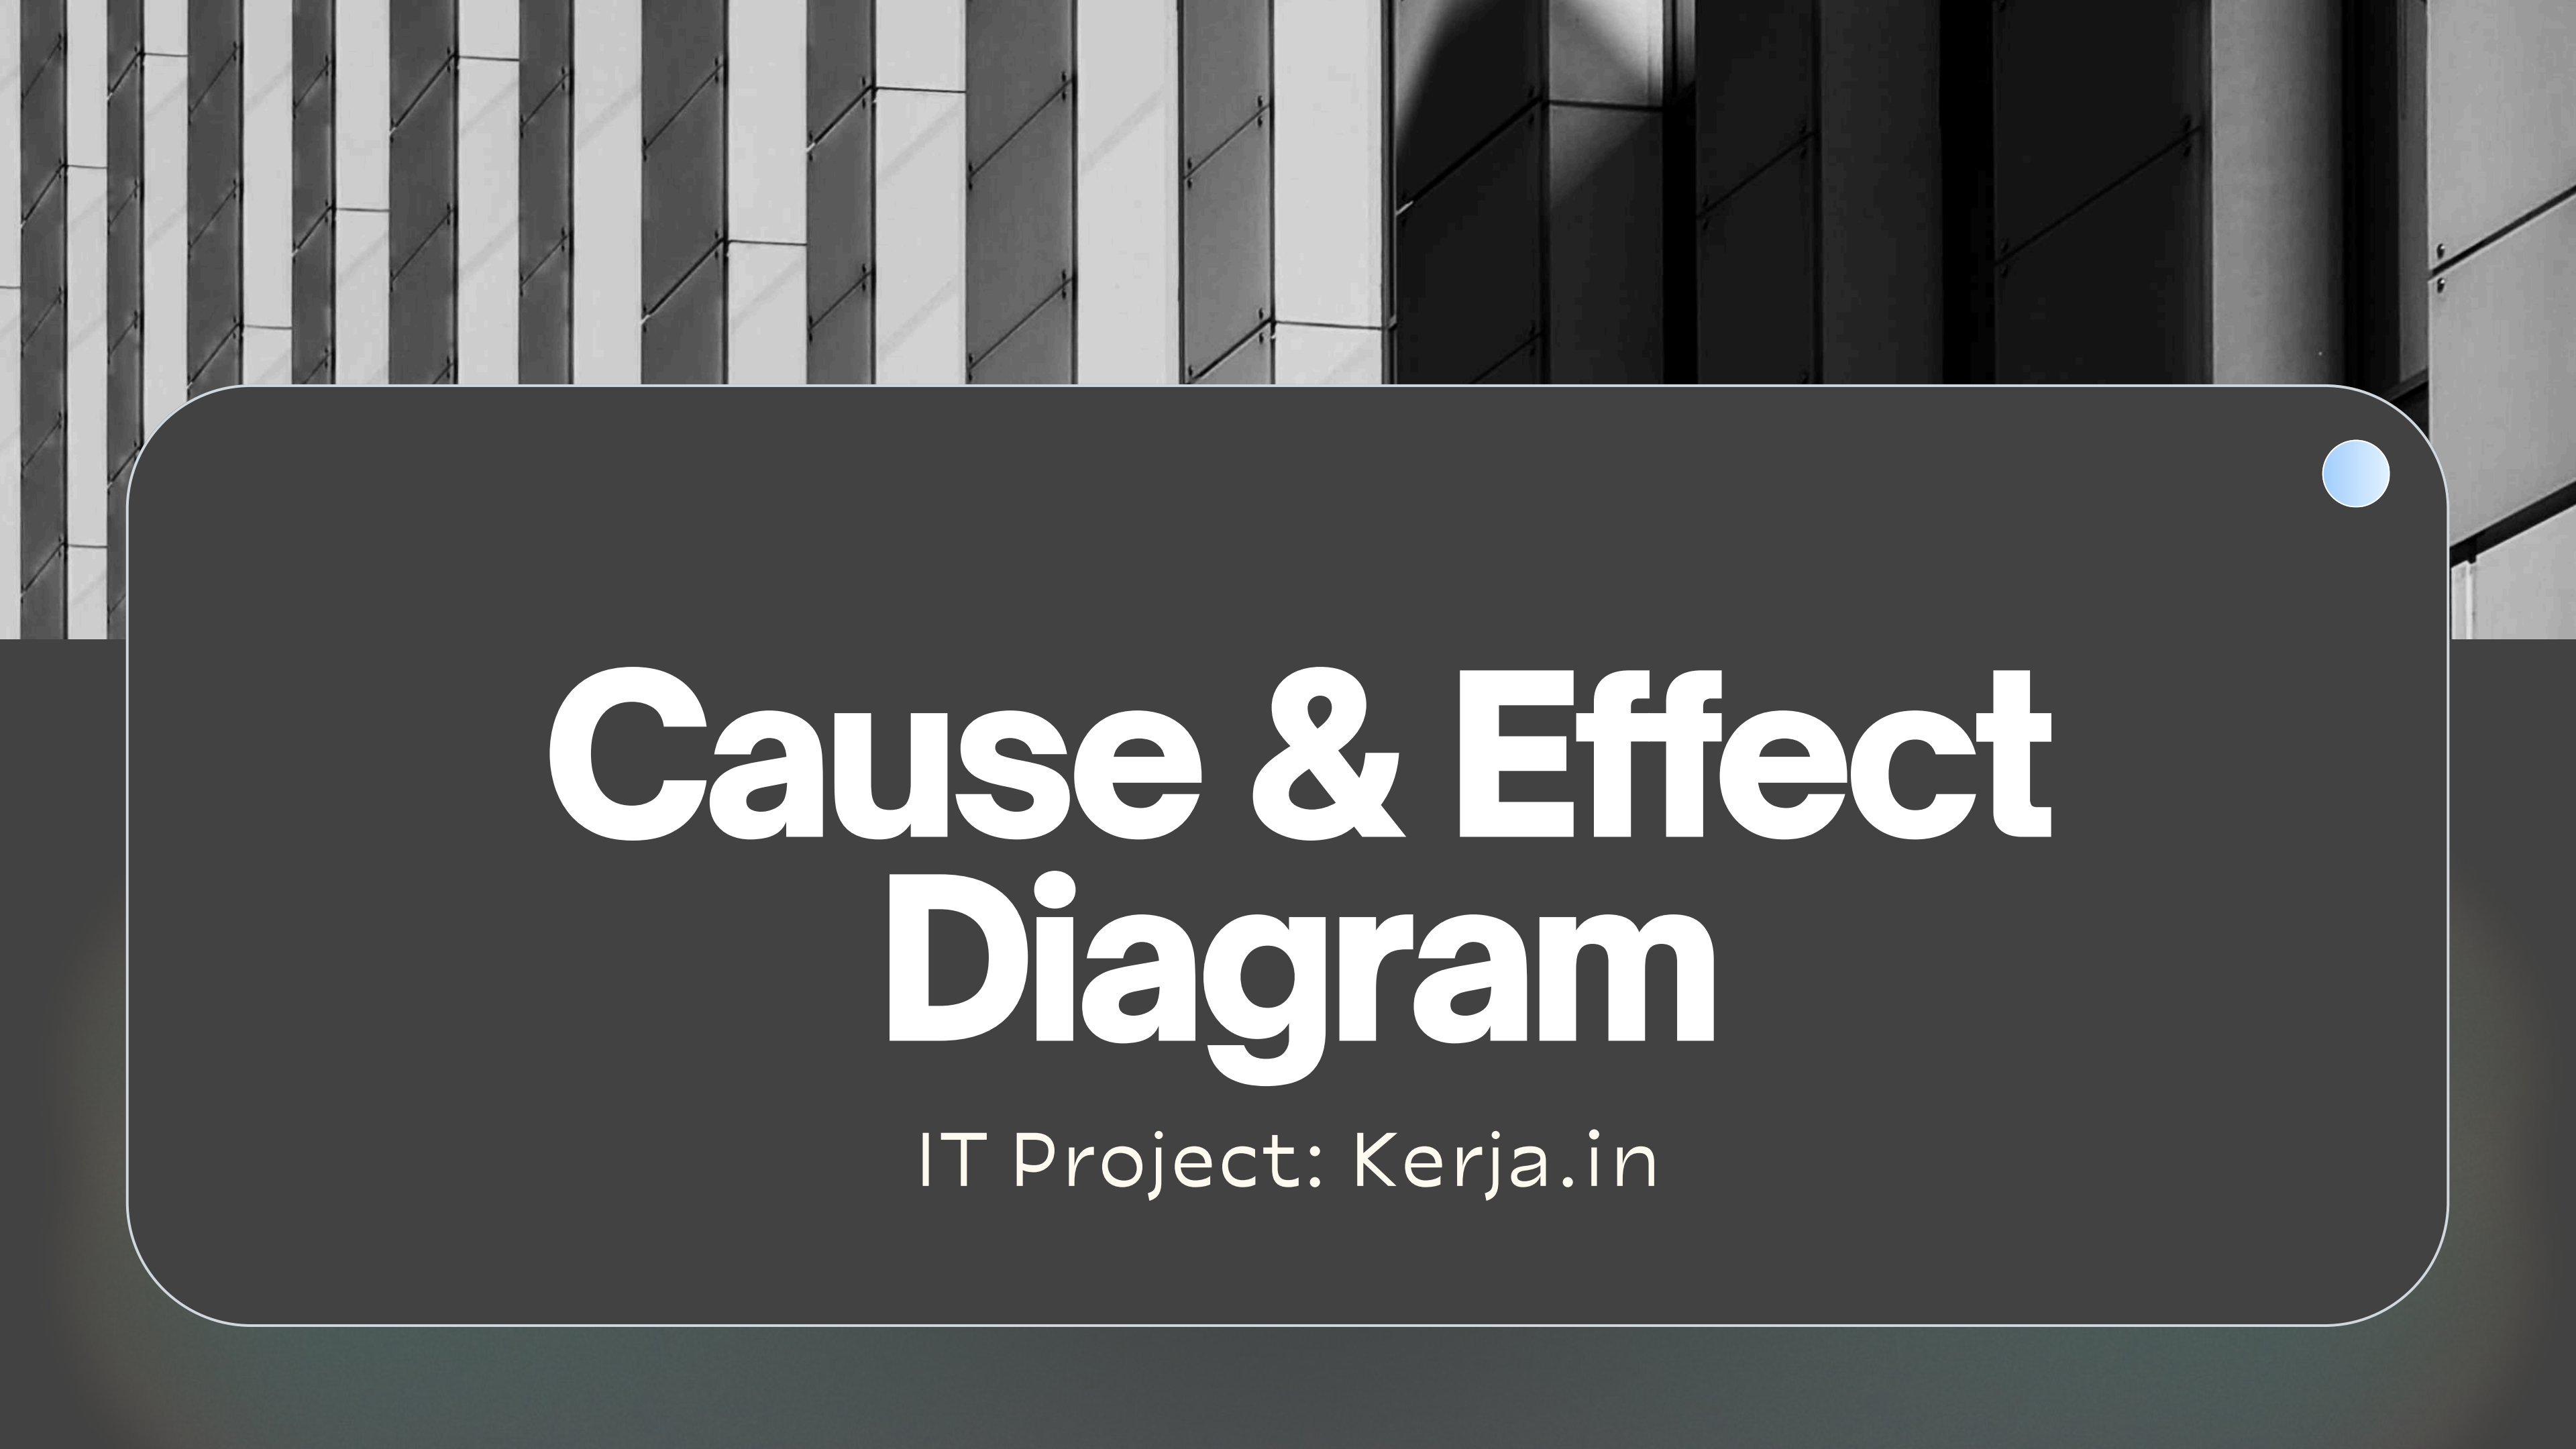

Cause & Effect Diagram

IT Project: Kerja.in

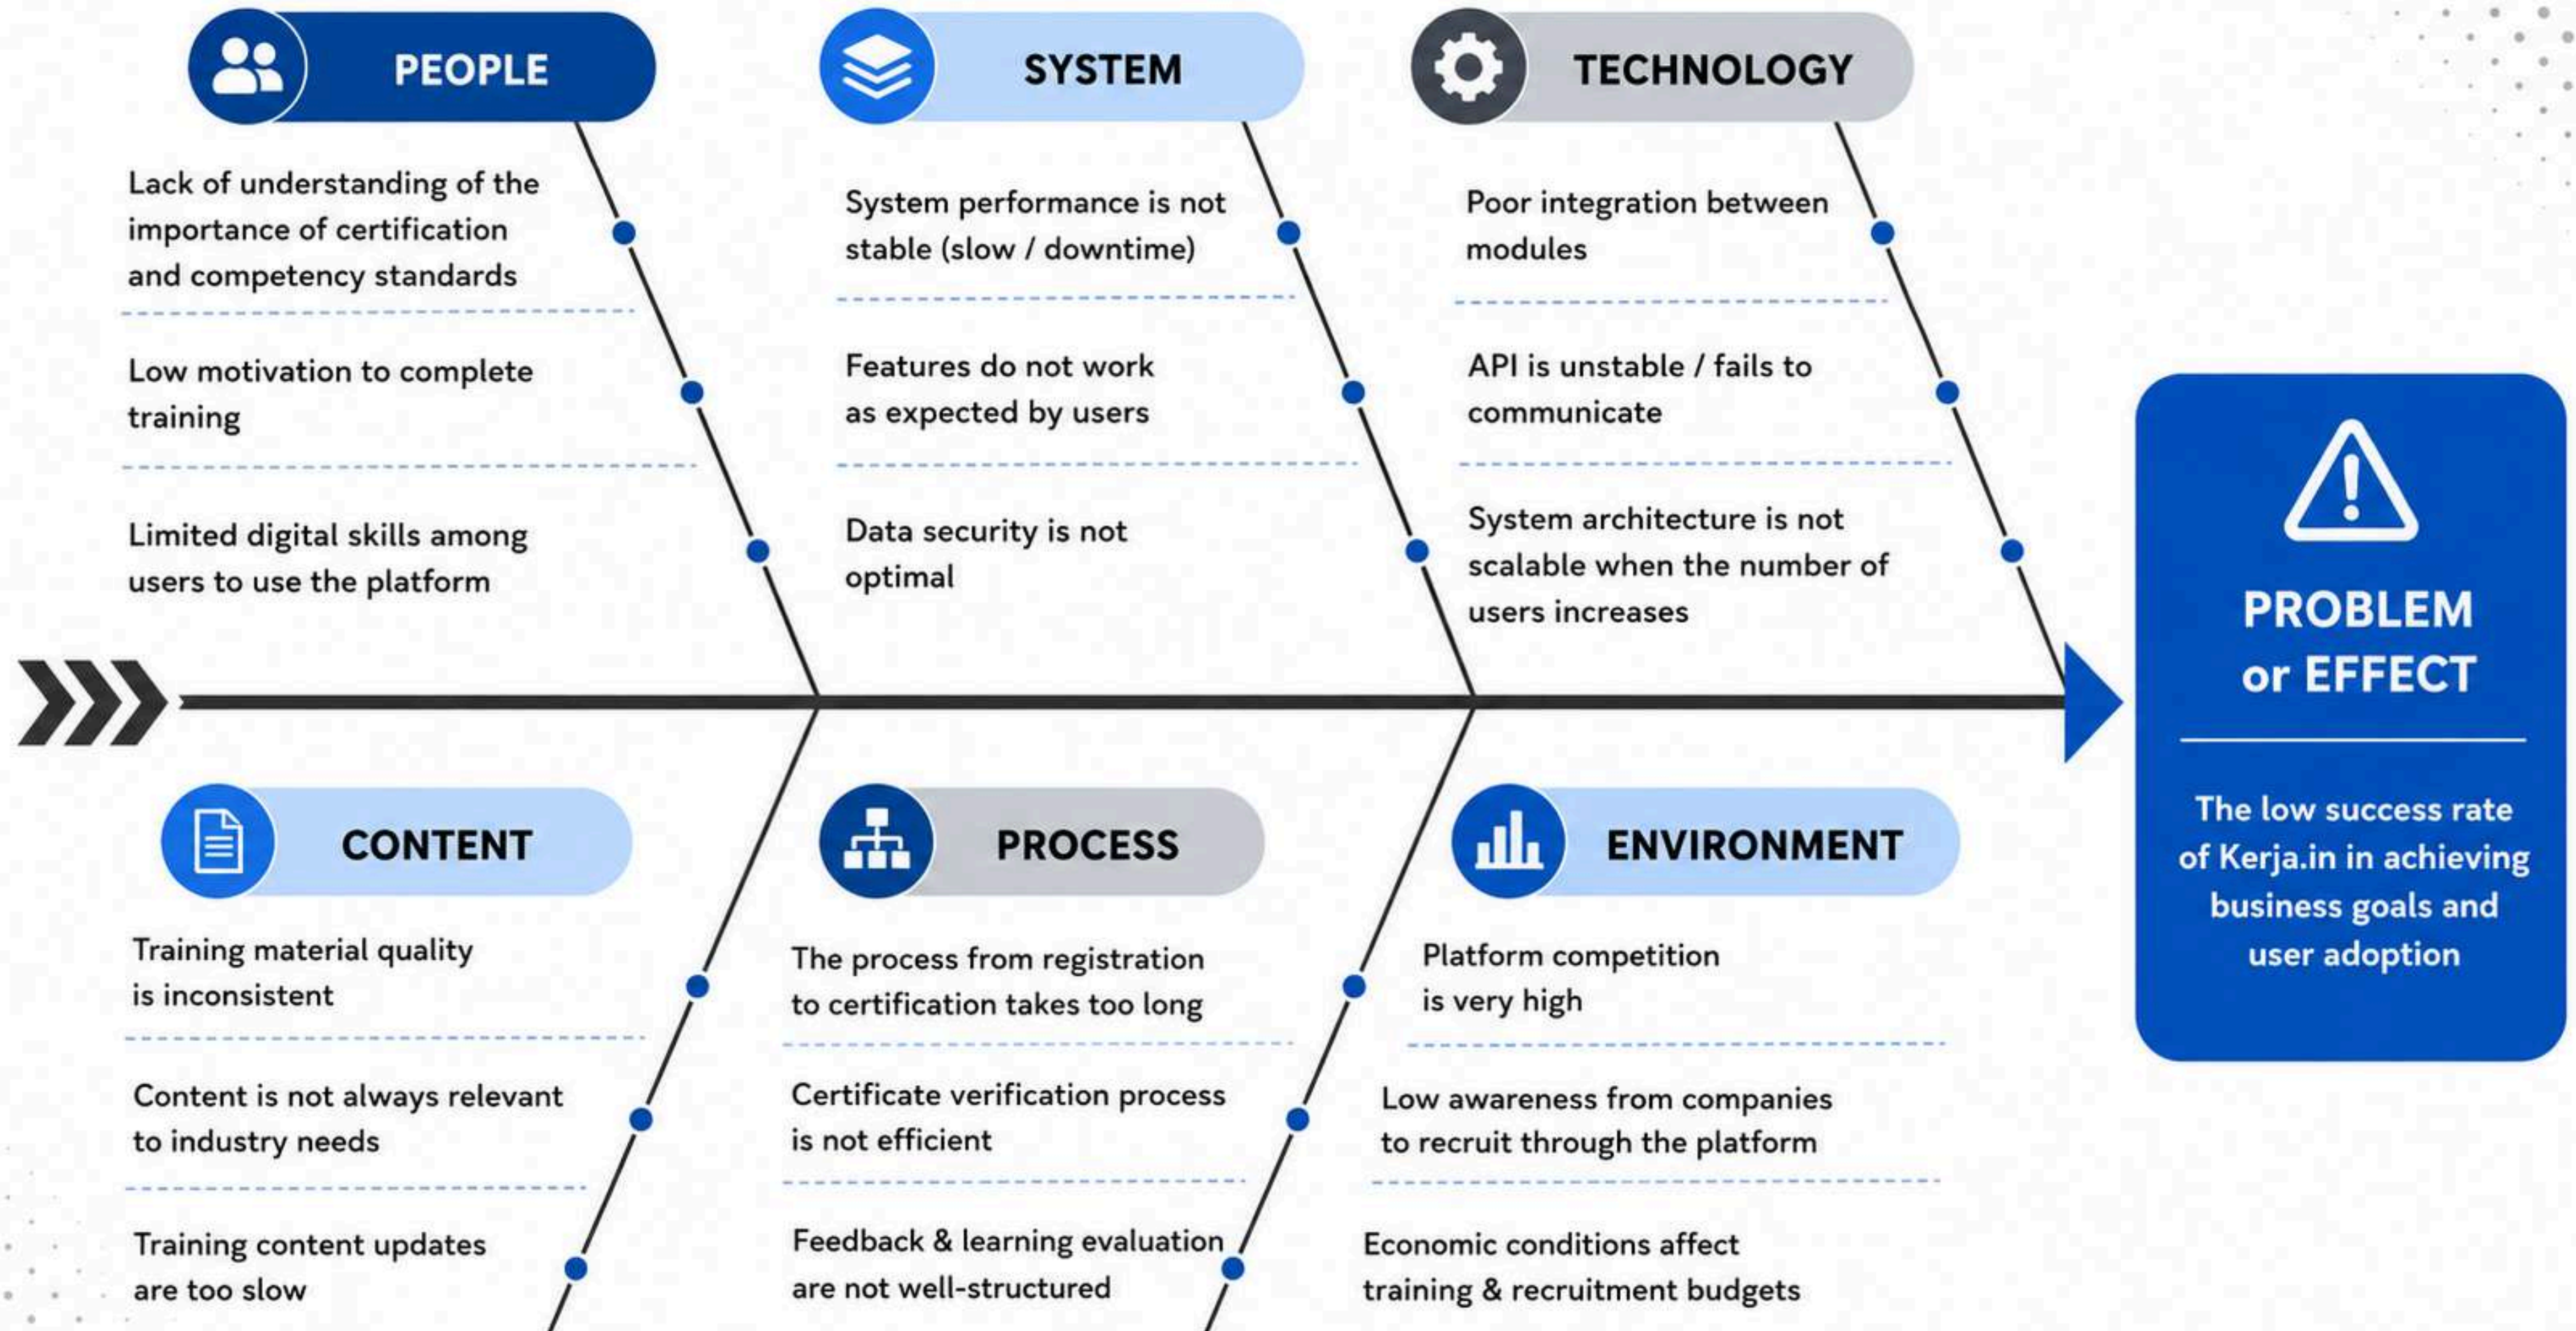

Link Video Youtube

<https://drive.google.com/file/d/1r2oDt9gpW1D-2ZTAhg4Dh11eQ1LZorgk/view?usp=drivesdk>

Thank You

for your time
and attention

 +123-456-7890

 www.reallygreatsite.com

 hello@reallygreatsite.com

 123 Anywhere St., Any City, ST 12345



Today's Agenda

- 01** Introduction
- 02** Problem Statement
- 03** Our Innovative Solutions
- 04** Discover Our Services
- 05** Size of Market
- 06** Direct & Indirect Competitor
- 07** Key Competitive Advantages
- 08** Traction
- 09** Accomplishments Date
- 10** Use of Funds
